

ID		Aktivitetsr	Aktivitetsnavn	Varighet	Start	Slutt	Foregående aktiviteter	22 27 april 2025 01 06 11 16 21 26 mai 2025 01 06 11 16 21 26 juni 2025 31 05 10 15																					
1																													
2			Totalt prosjekt	174 dager	ma 24.03.25	ma 01.12.25																							
3																													
4																													
5			Gråkammen 10D	74 dager	ma 24.03.25	ma 14.07.25																							
6			Opprigg	10 dager	ma 24.03.25	fr 04.04.25																							
7			Rivearbeider	10 dager	ma 07.04.25	ti 29.04.25	6																						
8			Undertaksbelegg, sløyfer og lekter	15 dager	on 23.04.25	ti 13.05.25	7SS+5 dager																						
9			Nye vindskier	3 dager	on 14.05.25	fr 16.05.25	8																						
10			Takstein	5 dager	on 14.05.25	ti 20.05.25	8																						
11			Blikkenslagerarbeider	6 dager	on 14.05.25	on 21.05.25	8																						
12			Komplettering	14 dager	on 18.06.25	ma 07.07.25	10																						
13			Ferdigbefaring	1 dag	to 05.06.25	to 05.06.25																							
14			Nedrigg	5 dager	ti 08.07.25	ma 14.07.25	12																						
15																													
16			Gråkammen 10C	51 dager	fr 16.05.25	fr 25.07.25																							
17			Opprigg	10 dager	fr 16.05.25	to 29.05.25	11SS+2 dager																						
18			Rivearbeider	11 dager	fr 30.05.25	fr 13.06.25	17																						
19			Avretning av eksist. tak	7 dager	ma 16.06.25	ti 24.06.25	18																						
20			Undertaksbelegg, sløyfer og lekter	7 dager	on 25.06.25	to 03.07.25	19																						
21			Nye vindskier	3 dager	fr 04.07.25	ti 08.07.25	20																						
22			Takstein	5 dager	on 09.07.25	ti 15.07.25	21																						
23			Blikkenslagerarbeider	4 dager	fr 04.07.25	on 09.07.25	20																						
24			Velux Vindu montering	5 dager	on 02.07.25	ti 08.07.25																							
25			Komplettering	8 dager	on 09.07.25	fr 18.07.25	24																						
26			Ferdigbefaring	1 dag	on 16.07.25	on 16.07.25																							
27			Nedrigg	5 dager	ma 21.07.25	fr 25.07.25	26																						
28																													
29			Gråkammen 8A	53 dager	ma 21.07.25	on 01.10.25																							
30			Opprigg	10 dager	ma 21.07.25	fr 01.08.25																							
31			Rivearbeider	11 dager	ma 04.08.25	ma 18.08.25	30																						
32			Avretning av eksist. Tak	5 dager	ti 19.08.25	ma 25.08.25	31																						
33			Undertaksbelegg, sløyfer og lekter	16 dager	to 14.08.25	to 04.09.25	31SS+8 dager																						
34			Takstein	5 dager	to 28.08.25	on 03.09.25	33SS+10 dager																						
35			Nye vindskier	3 dager	to 04.09.25	ma 08.09.25	34																						
36			Blikkenslagerarbeider	4 dager	fr 05.09.25	on 10.09.25	33																						
37			Komplettering	4 dager	to 18.09.25	ti 23.09.25	34																						
38			Ferdigbefaring	1 dag	on 24.09.25	on 24.09.25	37																						
39			Nedrigg	5 dager	to 25.09.25	on 01.10.25	38																						
40																													

Prosjekt: Fremdriftsplan - Gråka
Dato: on 08.10.25


Aktivitet

Deling

Milepæl

Sammendrag

Prosjektsammendrag











Inaktiv aktivitet

Inaktiv milepæl

Inaktivt sammendrag

Manuell aktivitet

Bare varighet











ID	1	Aktivitetsr	Aktivitetsnavn	Varighet	Start	Slutt	Foregående aktiviteter	2025																	
								22	27	april 2025		01	06	11	16	21	26	mai 2025		01	06	11	16	21	26
41			Gråkammen 8B	43 dager	fr 08.08.25	ti 07.10.25																			
42			Opprigg	10 dager	fr 08.08.25	to 21.08.25																			
43			Rivearbeider	11 dager	fr 22.08.25	fr 05.09.25	42																		
44			Avretting av Eksist. Tak	5 dager	ma 08.09.25	fr 12.09.25	43																		
45			Undertaksbelegg, sløyfer og lekter	16 dager	on 03.09.25	on 24.09.25	43SS+8 dager																		
46			Takstein	5 dager	on 17.09.25	ti 23.09.25	45SS+10 dager																		
47			Nye vindskier	3 dager	on 24.09.25	fr 26.09.25	46																		
48			Blikkenslagerarbeider	4 dager	to 25.09.25	ti 30.09.25	45																		
49			Komplettering	4 dager	on 24.09.25	ma 29.09.25	46																		
50			Ferdigbefaring	1 dag	ti 30.09.25	ti 30.09.25	49																		
51			Nedrigg	5 dager	on 01.10.25	ti 07.10.25	50																		
52																									
53			Gråkammen 10E	45 dager	to 18.09.25	on 19.11.25																			
54			Opprigg	10 dager	to 18.09.25	on 01.10.25																			
55			Rivearbeider	11 dager	ma 06.10.25	ma 20.10.25	50																		
56			Avretting av Eksist Tak	5 dager	to 16.10.25	on 22.10.25	55																		
57			Undertaksbelegg, sløyfer og lekter	16 dager	to 16.10.25	to 06.11.25	55SS+8 dager																		
58			Takstein	5 dager	to 30.10.25	on 05.11.25	57SS+10 dager																		
59			Nye vindskier	3 dager	to 06.11.25	ma 10.11.25	58																		
60			Blikkenslagerarbeider	4 dager	fr 07.11.25	on 12.11.25	57																		
61			Komplettering	4 dager	to 06.11.25	ti 11.11.25	58																		
62			Ferdigbefaring	1 dag	on 12.11.25	on 12.11.25	61																		
63			Nedrigg	5 dager	to 13.11.25	on 19.11.25	62																		
64																									
65			Gråkammen 10F	43 dager	to 02.10.25	ma 01.12.25																			
66			Opprigg	10 dager	to 02.10.25	on 15.10.25	54																		
67			Rivearbeider	11 dager	ma 13.10.25	ma 27.10.25																			
68			Avretning av eksist tak	6 dager	fr 31.10.25	fr 07.11.25	67																		
69			Undertaksbelegg, sløyfer og lekter	16 dager	to 23.10.25	to 13.11.25	67SS+8 dager																		
70			Takstein	5 dager	to 06.11.25	on 12.11.25	69SS+10 dager																		
71			Nye vindskier	3 dager	ti 28.10.25	to 30.10.25	67																		
72			Blikkenslagerarbeider	4 dager	fr 14.11.25	on 19.11.25	69																		
73			Komplettering	4 dager	to 13.11.25	ti 18.11.25	70																		
74			Ferdigbefaring	1 dag	on 19.11.25	on 19.11.25	73																		
75			Nedrigg	5 dager	ti 25.11.25	ma 01.12.25																			

Prosjekt: Fremdriftsplan - Gråka
Dato: on 08.10.25

Aktivitet		Inaktiv aktivitet		Manuell sammendragsfremheving		Ekstern milepæl	
Deling		Inaktiv milepæl		Manuelt sammendrag		Tidsfrist	
Milepæl		Inaktivt sammendrag		Bare start		Fremdrift	
Sammendrag		Manuell aktivitet		Bare slutt		Manuell fremdrift	
Prosjektsammendrag		Bare varighet		Eksterne aktiviteter			

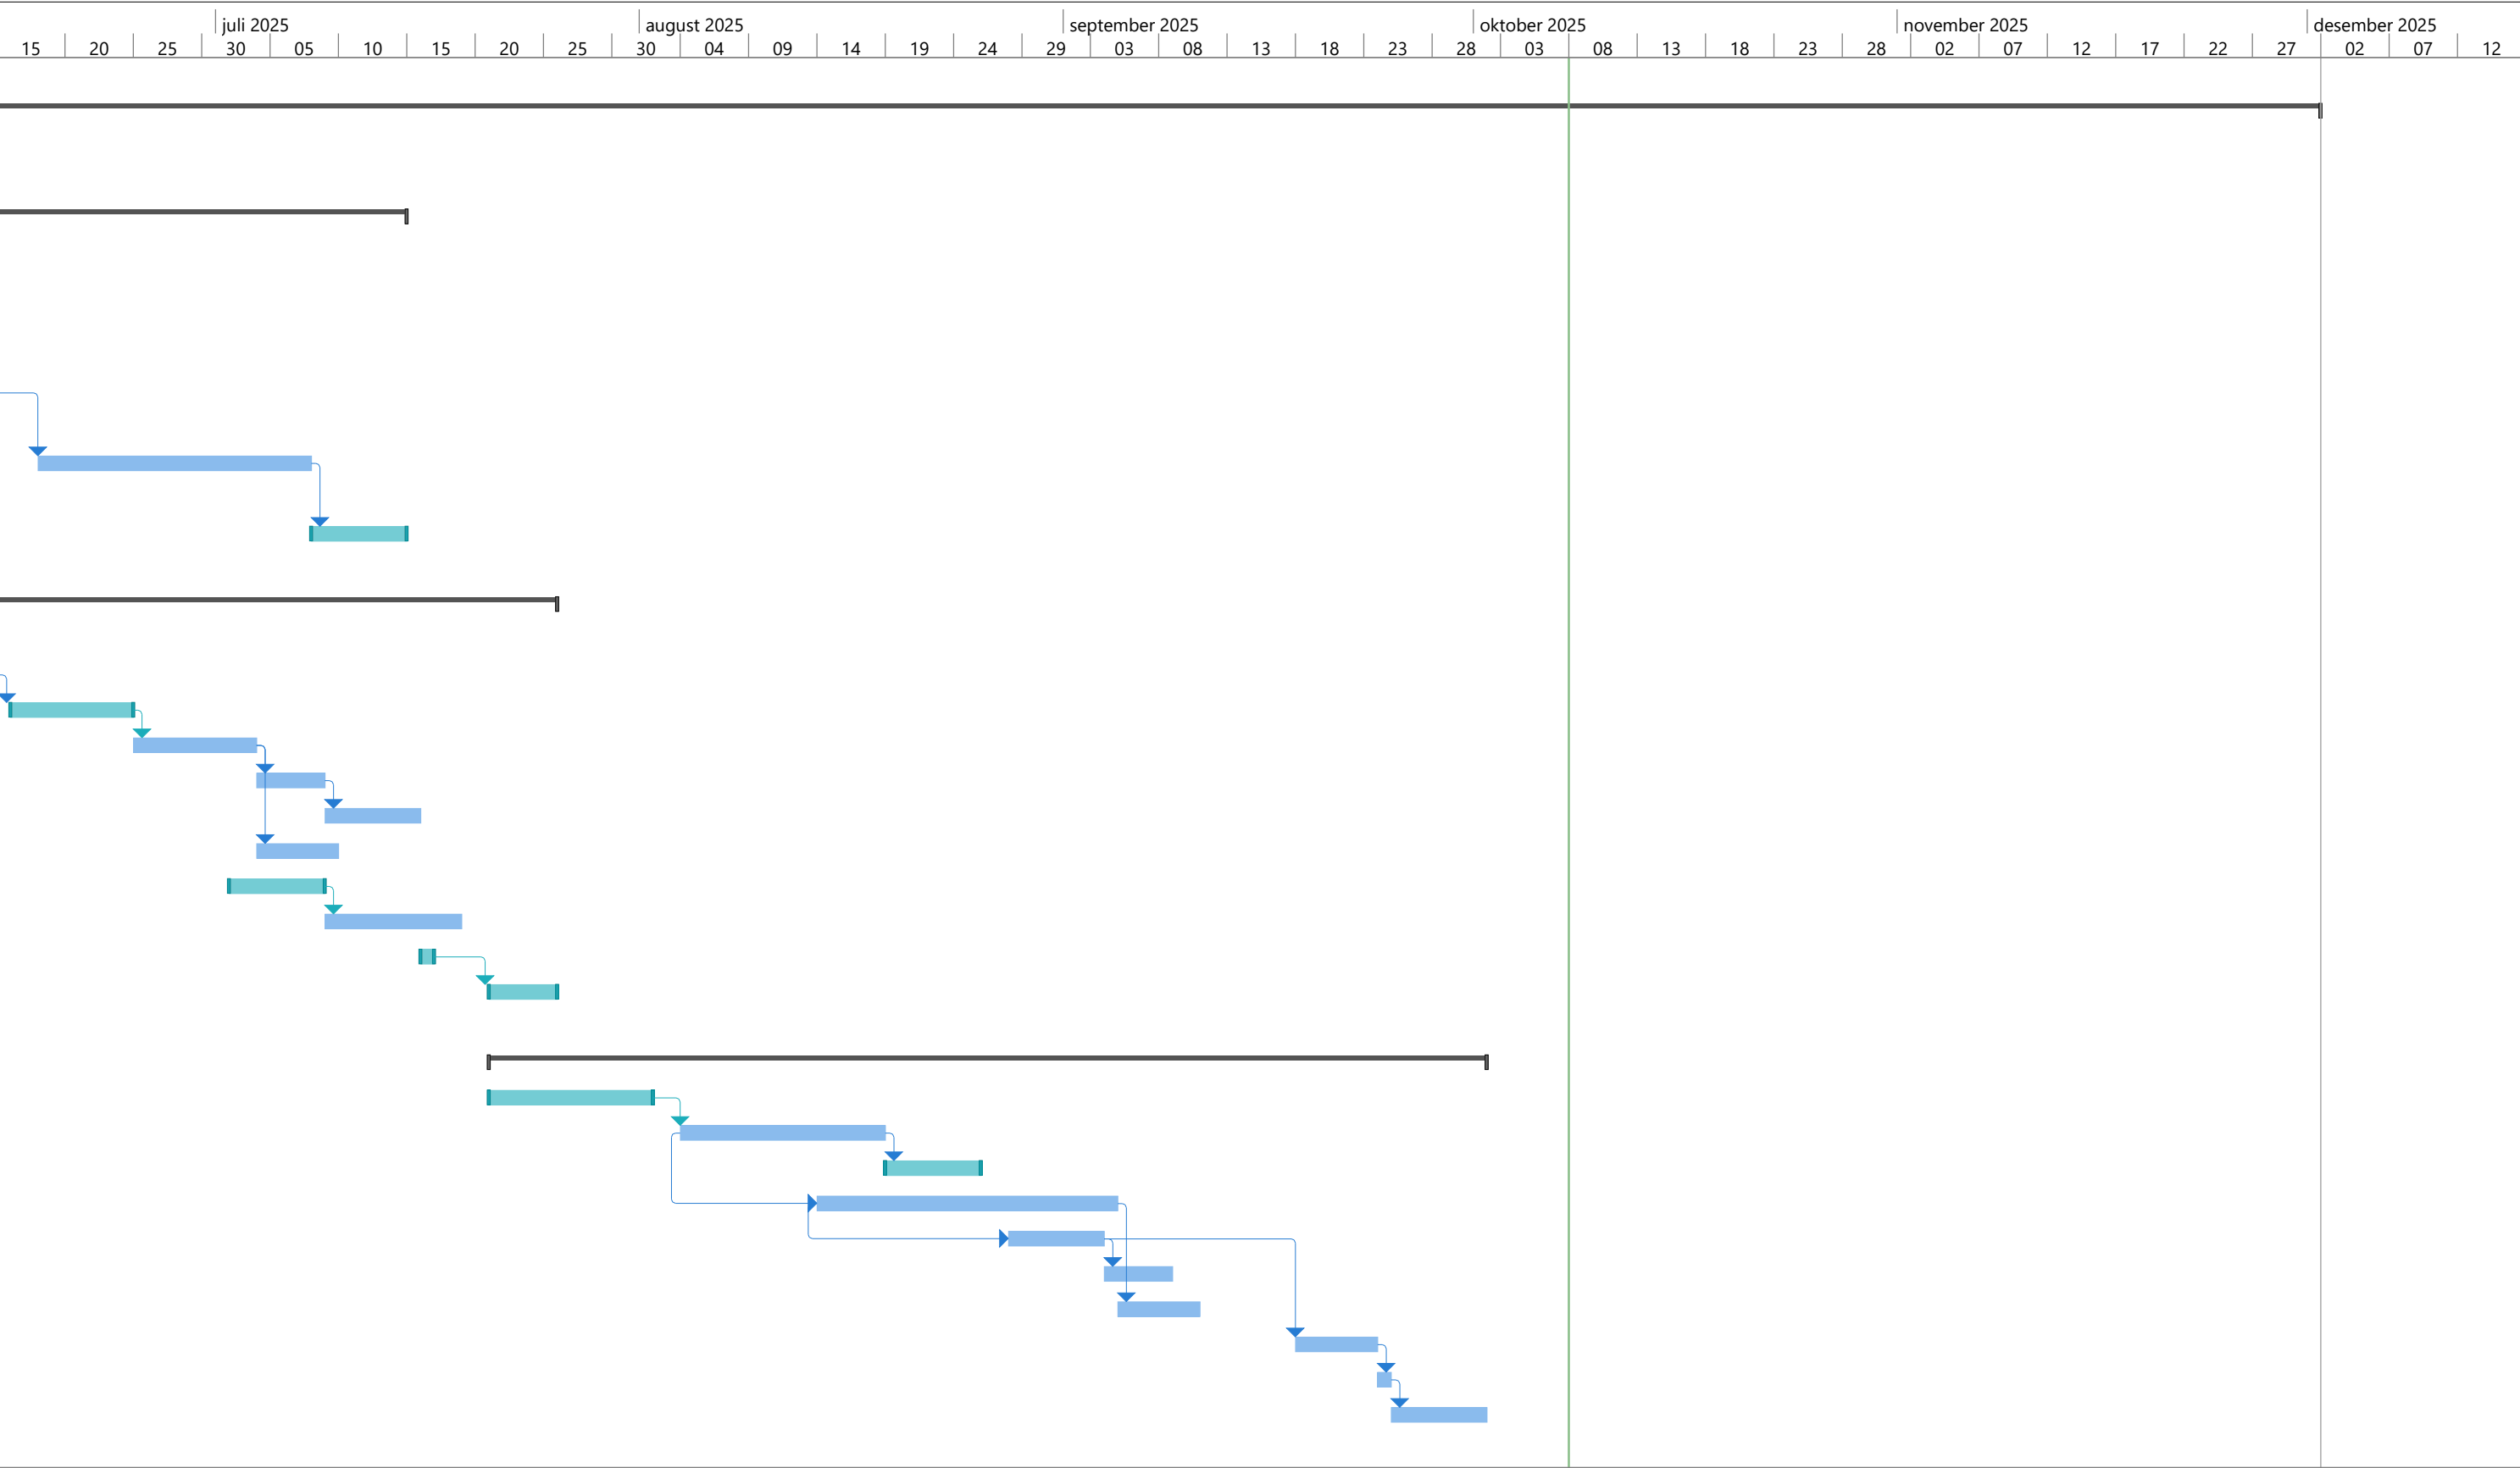

Prosjekt: Fremdriftsplan - Gråka Dato: on 08.10.25	Aktivitet		Inaktiv aktivitet		Manuell sammendragsfremheving		Ekstern milepæl	
	Deling		Inaktiv milepæl		Manuelt sammendrag		Tidsfrist	
	Milepæl		Inaktivt sammendrag		Bare start		Fremdrift	
	Sammendrag		Manuell aktivitet		Bare slutt		Manuell fremdrift	
	Prosjektsammendrag		Bare varighet		Eksterne aktiviteter			

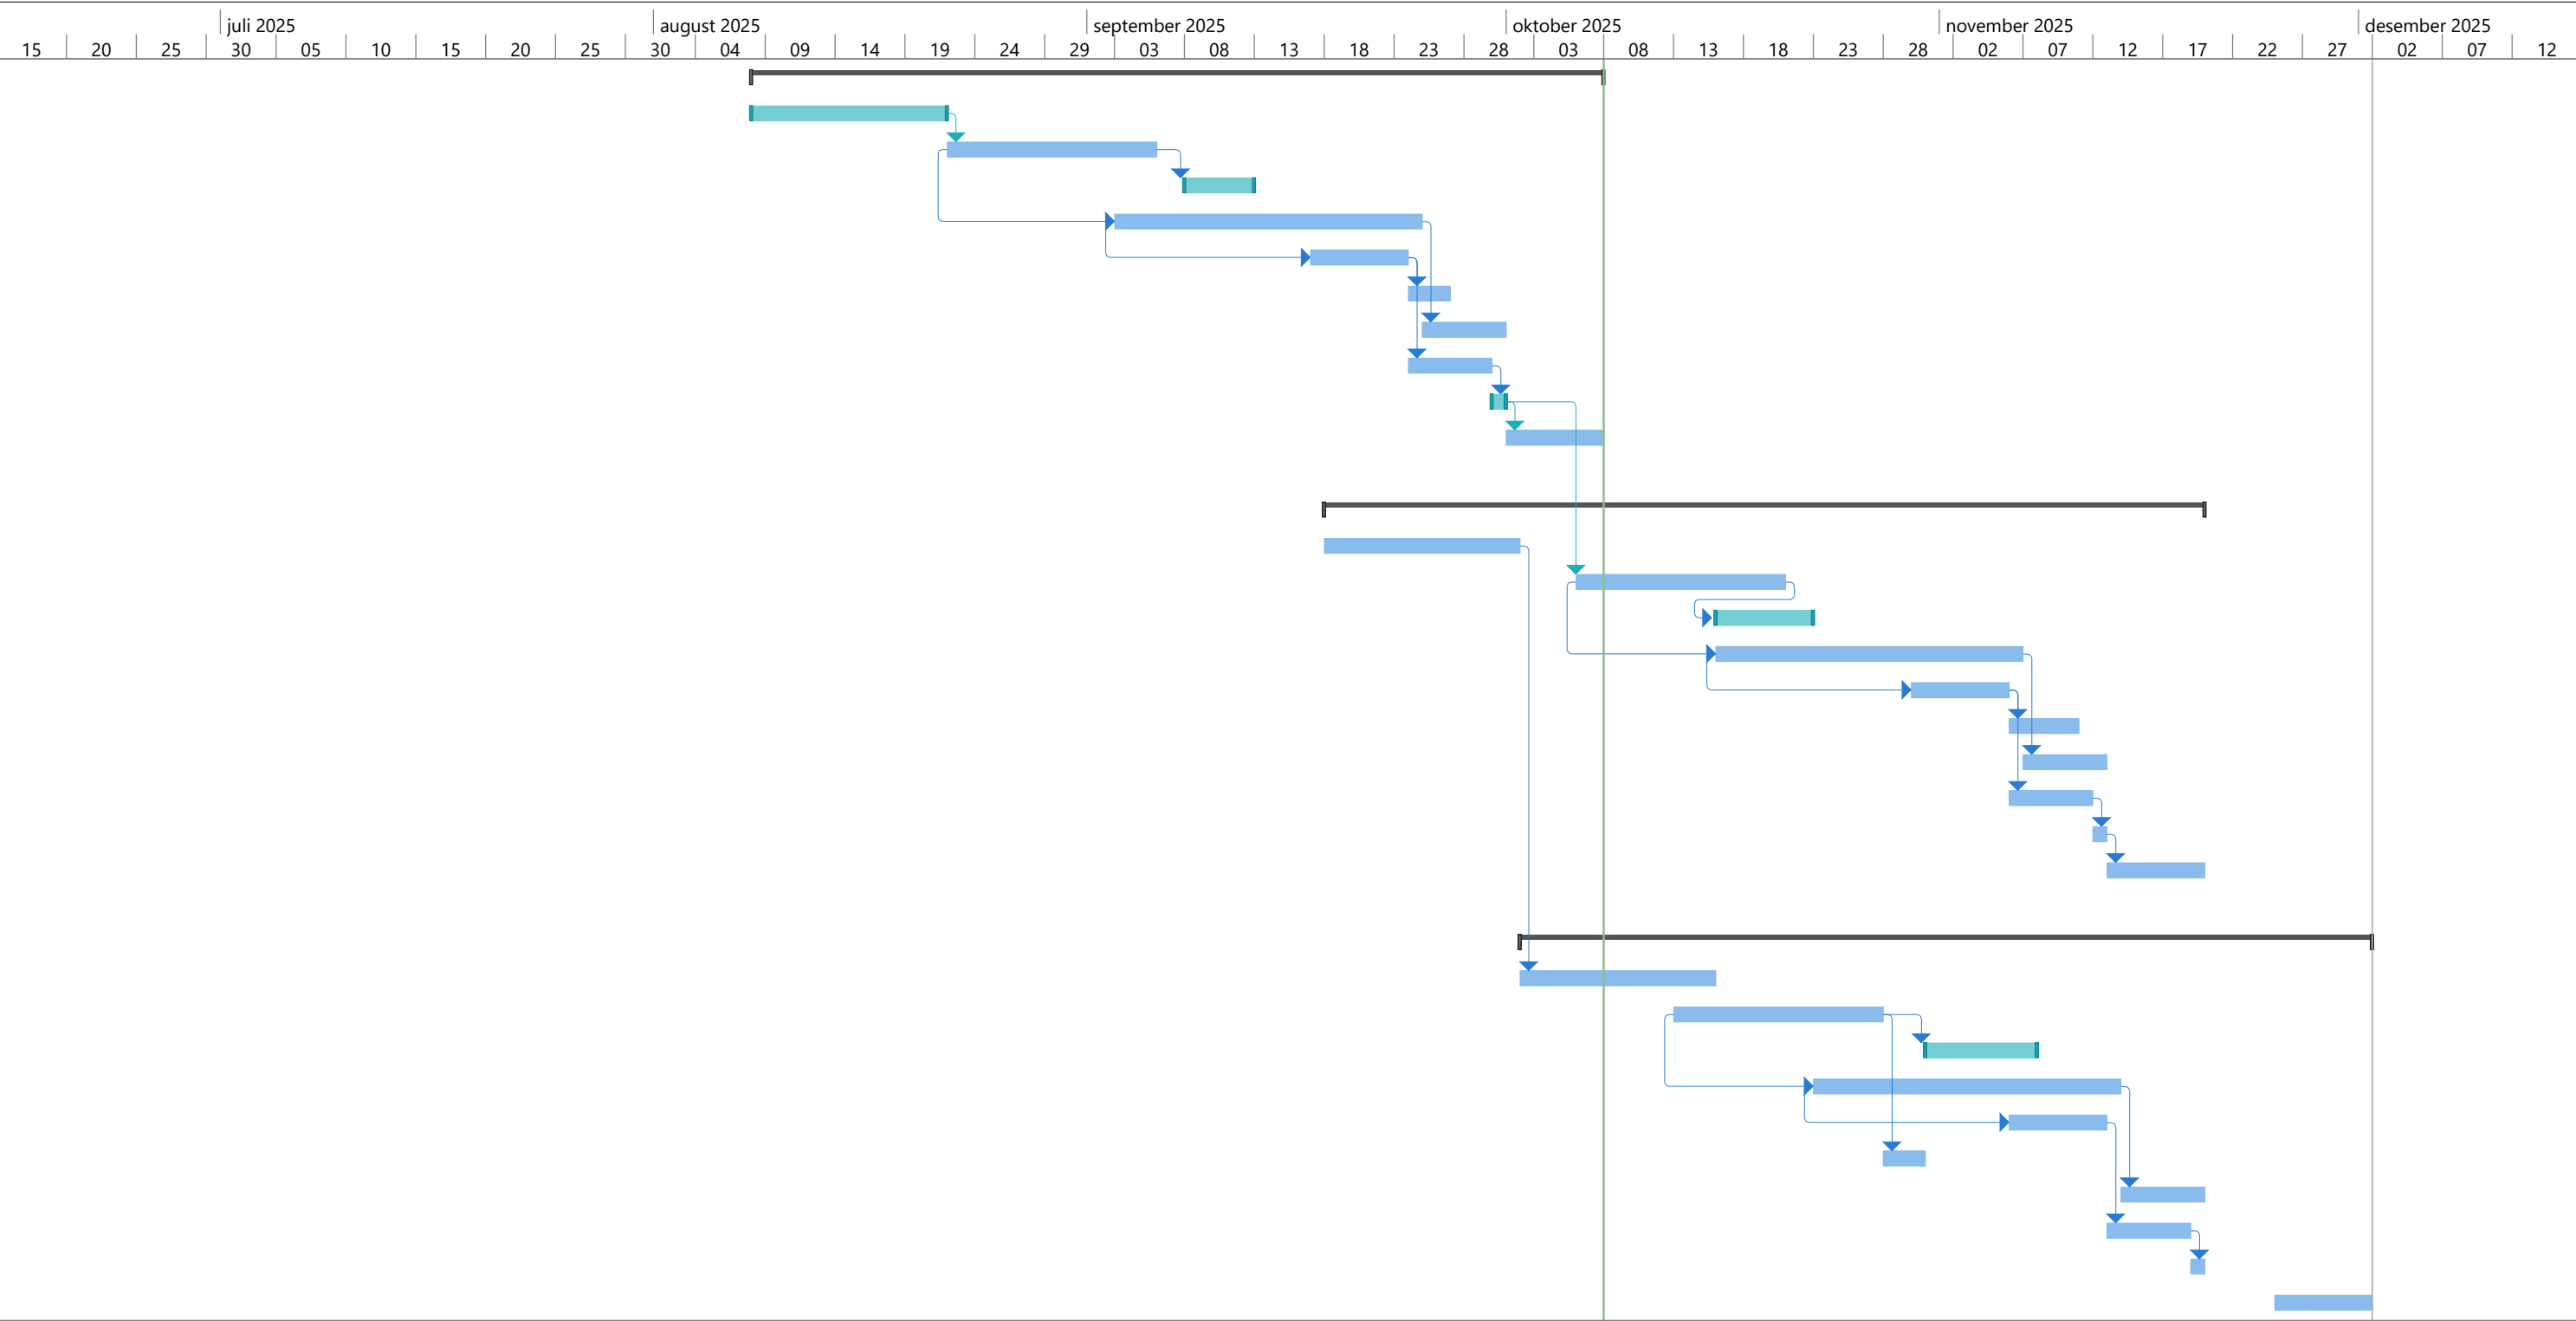

Prosjekt: Fremdriftsplan - Gråka Dato: on 08.10.25	Aktivitet		Inaktiv aktivitet		Manuell sammendragsfremheving		Ekstern milepæl	
	Deling		Inaktiv milepæl		Manuelt sammendrag		Tidsfrist	
	Milepæl		Inaktivt sammendrag		Bare start		Fremdrift	
	Sammendrag		Manuell aktivitet		Bare slutt		Manuell fremdrift	
	Prosjektsammendrag		Bare varighet		Eksterne aktiviteter			



Prosjekt: Fremdriftsplan - Gråka
Dato: on 08.10.25

Aktivitet

Deling

Milepæl

Sammendrag

Prosjektsammendrag

Inaktiv aktivitet

Inaktiv milepæl

Inaktivt sammendrag

Manuell aktivitet

Bare varighet

Manuell sammendragsfremheving

Manuelt sammendrag

Bare start

Bare slutt

Eksterne aktiviteter

Ekstern milepæl

Tidsfrist

Fremdrift

Manuell fremdrift



Prosjekt: Fremdriftsplan - Gråka
Dato: on 08.10.25

Aktivitet

Deling

Milepæl

Sammendrag

Prosjektsammendrag

Inaktiv aktivitet

Inaktiv milepæl

Inaktivt sammendrag

Manuell aktivitet

Bare varighet

Manuell sammendrag

Bare start

Bare slutt

Eksterne aktiviteter

Ekstern milepæl

Tidsfrist

Fremdrift

Manuell fremdrift
